

**UCSD FIRE STATION**

**Milestones & Summary**

Activity ID	Activity Name	Original Duration	Start	Finish
MS1000	Notice-to-Proceed (NTP)	0	23-Mar-20	
MS1010	Mobilization	10	23-Mar-20	03-Apr-20
MS1020	Demolition & Excavation	35	23-Mar-20	08-May-20
MS1025	Critical Phase Grading	10	11-May-20	22-May-20
MS1030	Site Grading & Improvements	50	11-May-20	20-Jul-20
MS1040	Building Structure	54	26-May-20	07-Aug-20
MS1050	Traffic Improvements	35	11-May-20	29-Jun-20
MS1060	Weather Allowance	5	10-Aug-20	14-Aug-20
MS1070	Completion of Work	0		14-Aug-20

**Mobilization**

Activity ID	Activity Name	Original Duration	Start	Finish
MOB1000	Metering & Tie-In	10	23-Mar-20	03-Apr-20

Activity ID	Activity Name	Original Duration	Start	Finish
MOB2000	Site Fencing & Barricades	3	23-Mar-20	25-Mar-20
MOB2010	Site Office Trailer Setup	5	30-Mar-20	03-Apr-20

**Demolition & Early Work**

Activity ID	Activity Name	Original Duration	Start	Finish
DE1000	Potholing & Layout	5	23-Mar-20	27-Mar-20
DE1010	Final Metering & Disconnect	5	23-Mar-20	27-Mar-20

Activity ID	Activity Name	Original Duration	Start	Finish
DE2000	Tennis Court, Fence, & Lights	7	26-Mar-20	03-Apr-20
DE2010	Clear & Grub	10	06-Apr-20	17-Apr-20
DE2020	Mass Excavation	15	20-Apr-20	08-May-20

Activity ID	Activity Name	Original Duration	Start	Finish
DE3000	Potholing & Layout	10	23-Mar-20	03-Apr-20
DE3010	Shut-Off Valves & Bypasses	10	06-Apr-20	17-Apr-20

**Site Improvements**

Activity ID	Activity Name	Original Duration	Start	Finish
SI1000	Building Layout	5	11-May-20	15-May-20
SI1010	Building Pad Grading	5	18-May-20	22-May-20
SI1020	Site Surveying	10	18-May-20	01-Jun-20
SI1030	Site Grading	15	26-May-20	15-Jun-20

Activity ID	Activity Name	Original Duration	Start	Finish
SI2000	Site Utilities	35	02-Jun-20	20-Jul-20

**Bio Basin**

Activity ID	Activity Name	Original Duration	Start	Finish
BB1000	Layout	5	02-Jun-20	08-Jun-20
BB1010	Excavation	5	09-Jun-20	15-Jun-20
BB1020	Install Pipe Section	5	16-Jun-20	22-Jun-20
BB1030	Material Infill	5	23-Jun-20	29-Jun-20

**Storm Drain**


Activity ID	Activity Name	Original Duration	Start	Finish
SD1000	Layout	5	09-Jun-20	15-Jun-20
SD1010	Trenching & Tie-In	10	16-Jun-20	29-Jun-20
SD1020	Pipe Install	15	23-Jun-20	13-Jul-20
SD1030	Backfill	5	14-Jul-20	20-Jul-20


**Sanitary Sewer**

Activity ID	Activity Name	Original Duration	Start	Finish
SS1000	Layout	5	16-Jun-20	22-Jun-20
SS1010	Trenching & Tie-In	5	23-Jun-20	29-Jun-20
SS1020	Pipe Install	5	30-Jun-20	06-Jul-20
SS1030	Backfill	5	07-Jul-20	13-Jul-20

**Domestic Waterline**

Activity ID	Activity Name	Original Duration	Start	Finish
SW1000	Layout	5	23-Jun-20	20-Jul-20

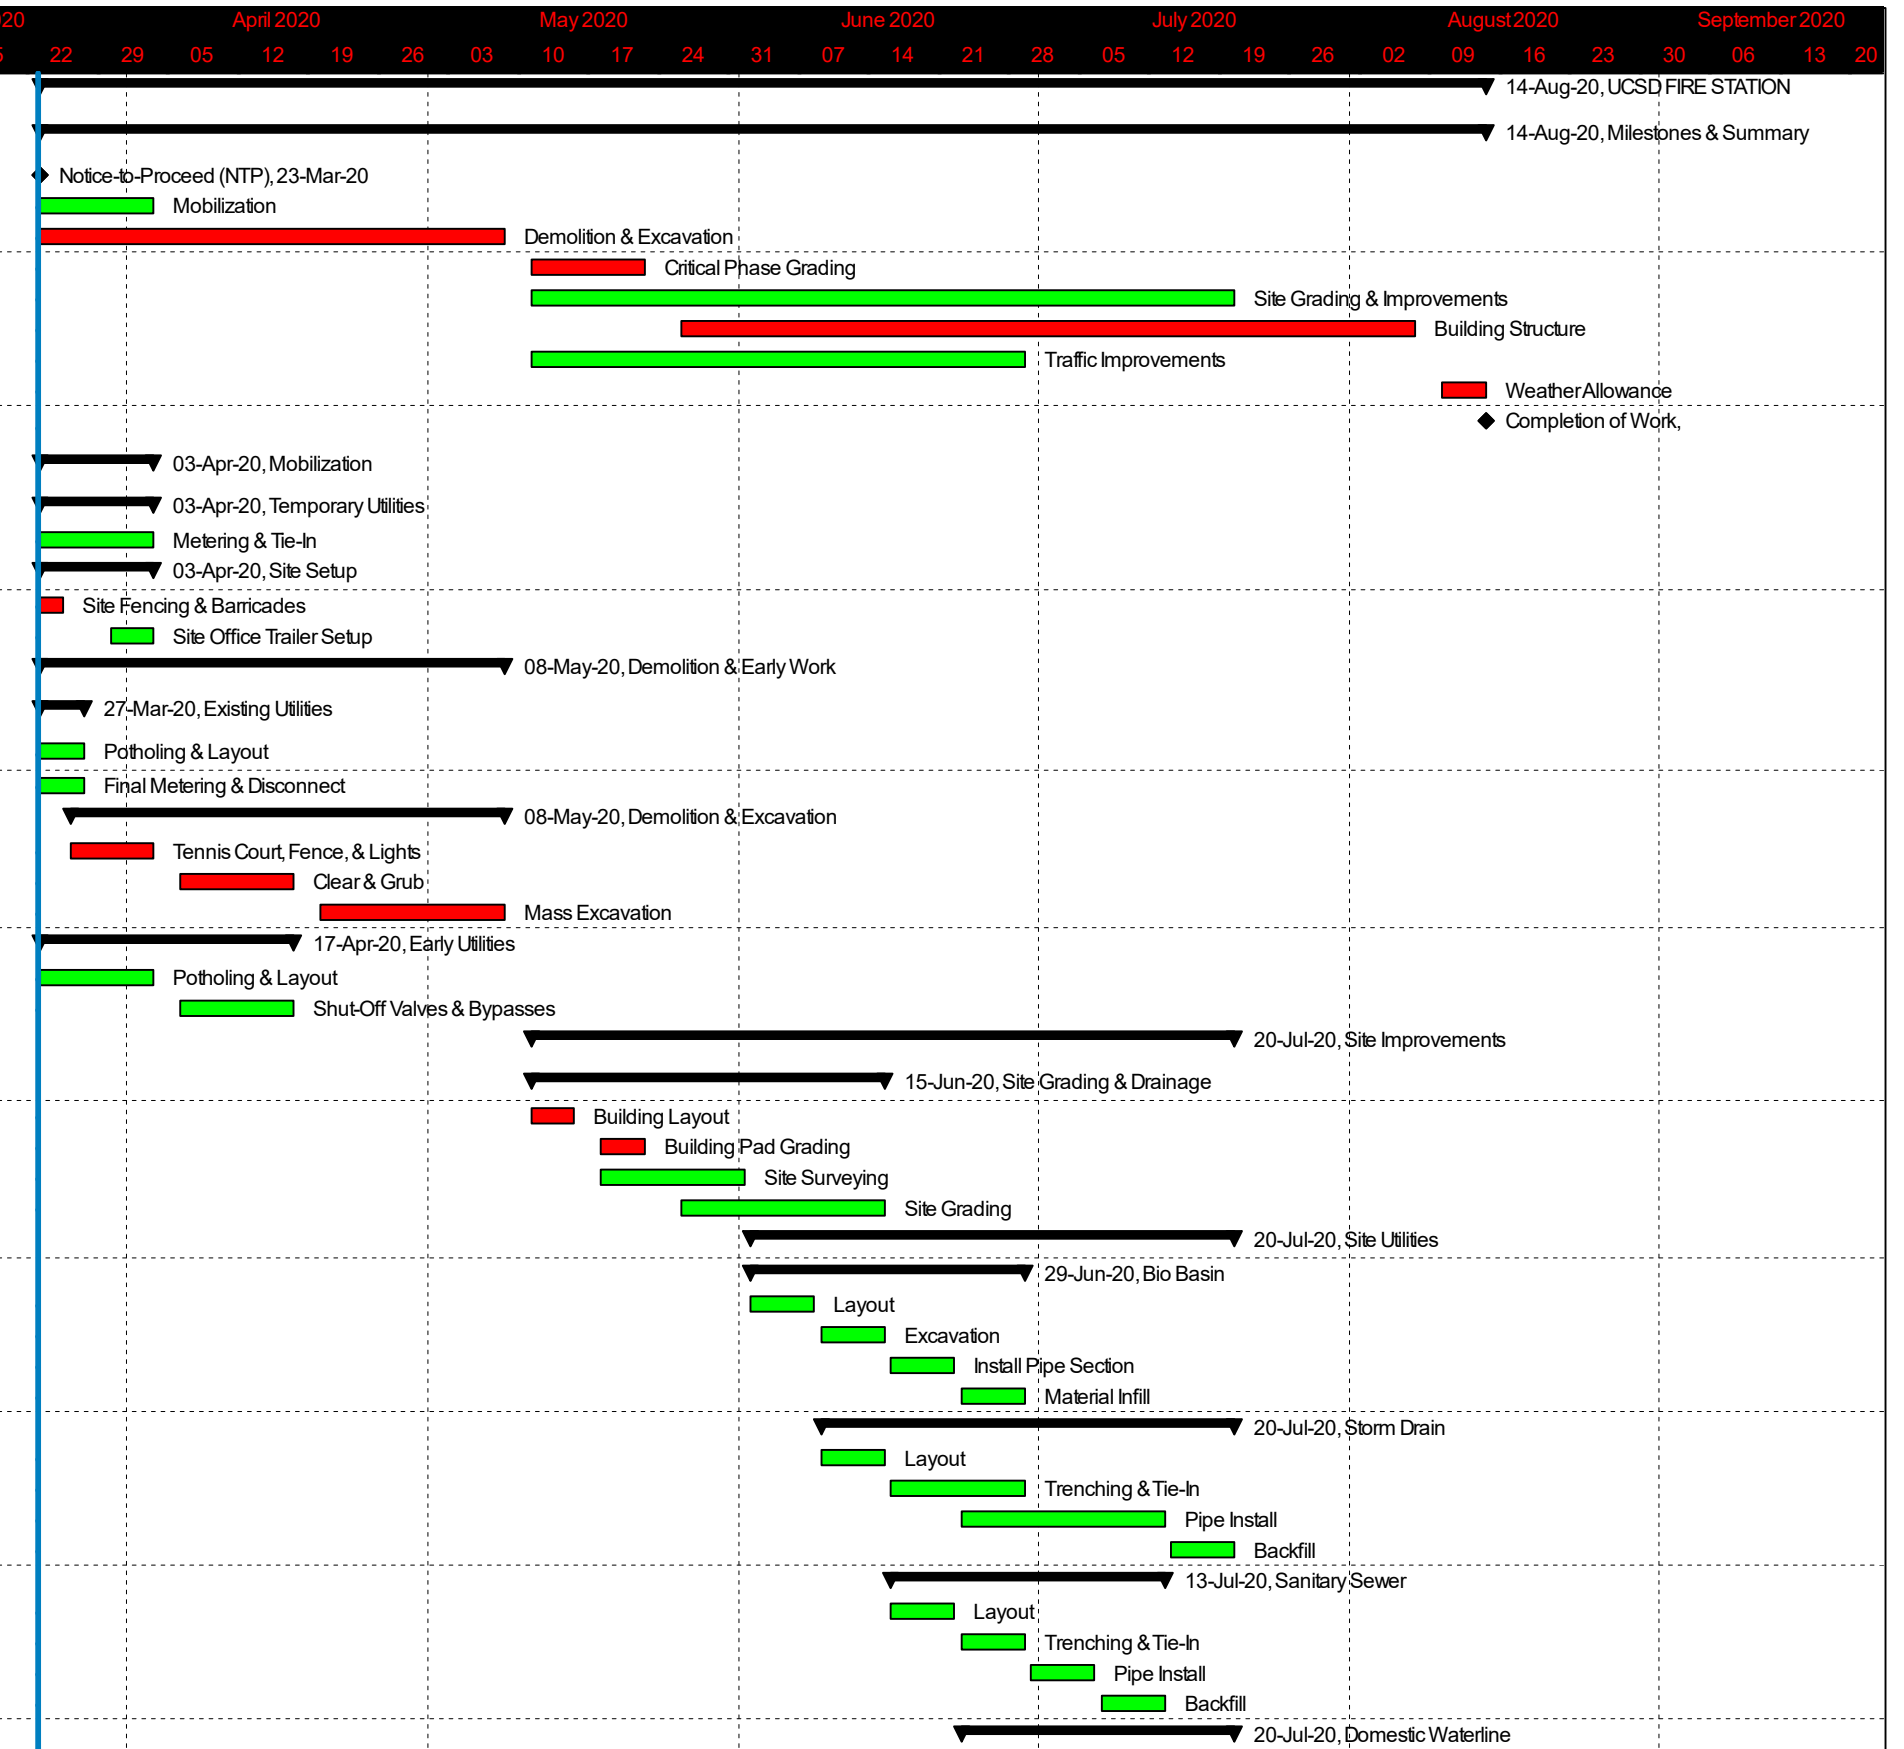

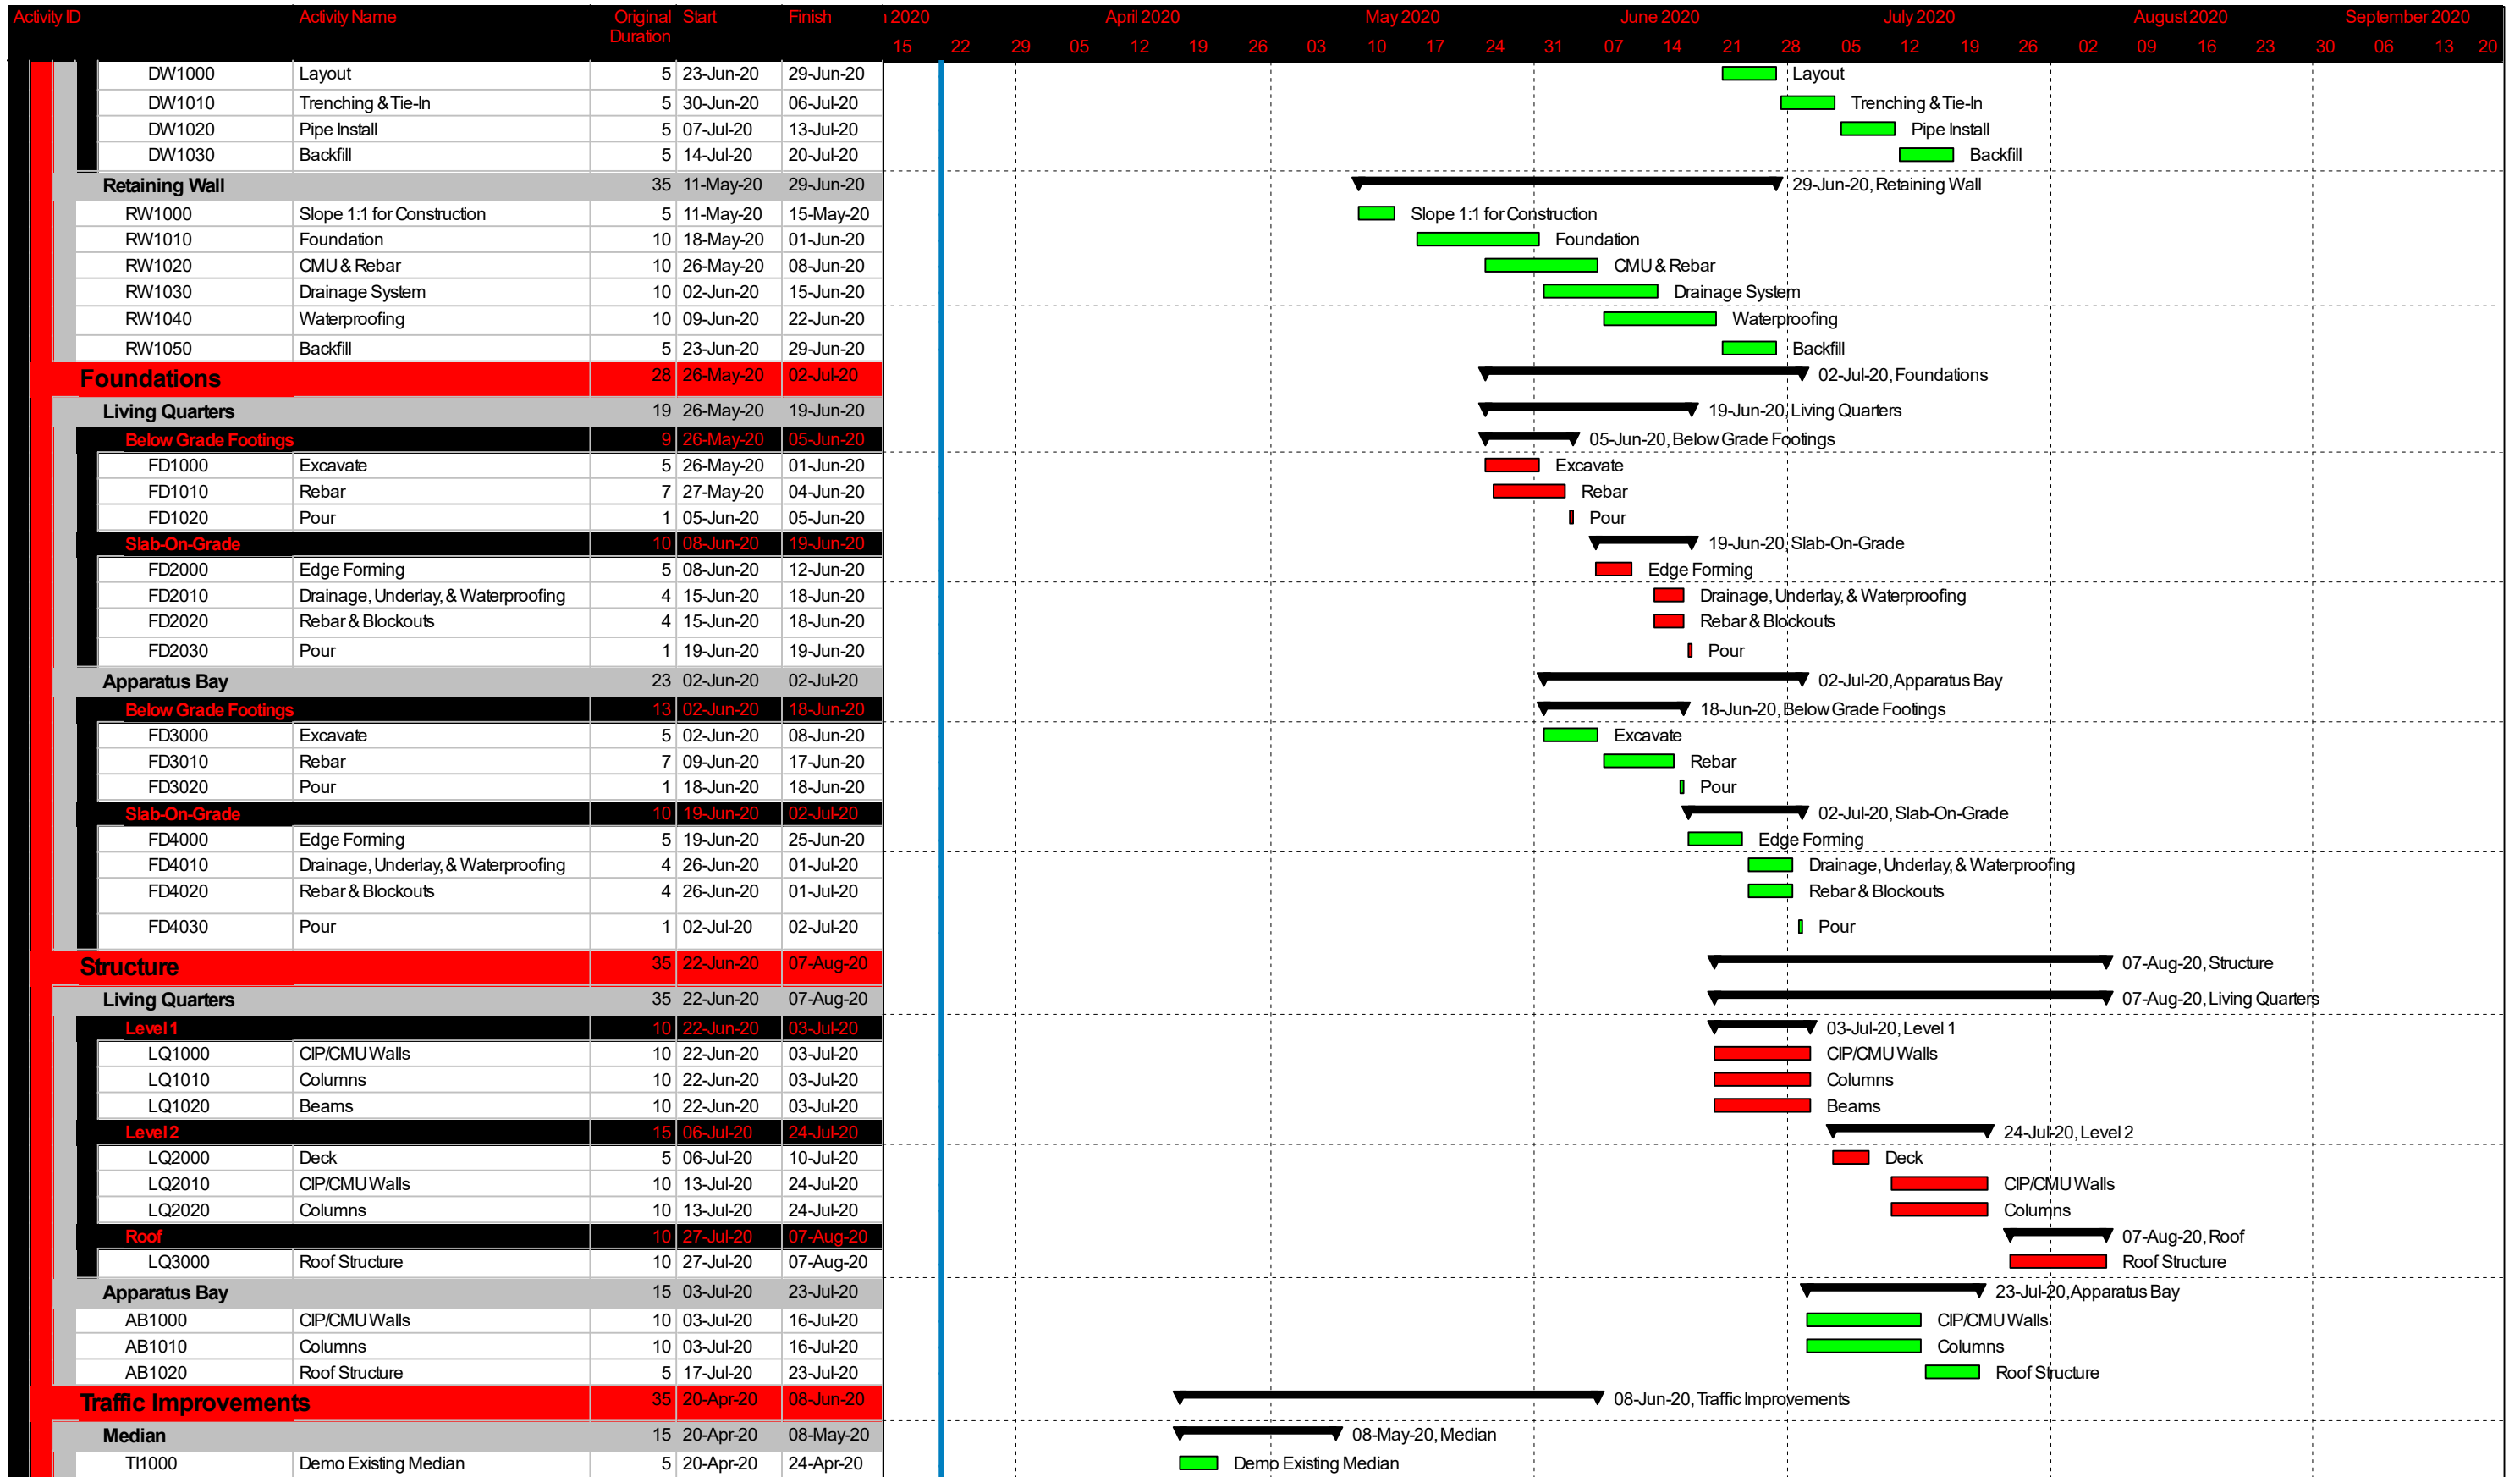

█ Actual Level of Effort   
 █ Remaining Work   
 ◆ Milestone  
█ Actual Work   
 █ Critical Remaining Work   
 ─ summary



